

APPENDIX 3
DEVELOPER COMMITMENTS

- 3-A Baseline Project Schedule
- 3-B Initial Transition and Phasing Plan (including Initial Construction Staging Plan)
- 3-C Initial Quality Management Plan
- 3-D Initial Health and Safety Plan
- 3-E Initial Environmental Management Plan
- 3-F Initial Project Management Plan
- 3-G Initial O&M Services Plan
- 3-H Key Contractors and Key Personnel
- 3-I Design & Construction Schedule of Values
- 3-J Physical Project Plan
- 3-K Form G-1

APPENDIX 3-A
BASELINE PROJECT SCHEDULE


(See attached.)

DEN Great Hall

*** Baseline View

Printed: 7/13/2017

Planned by Asta Powerproject

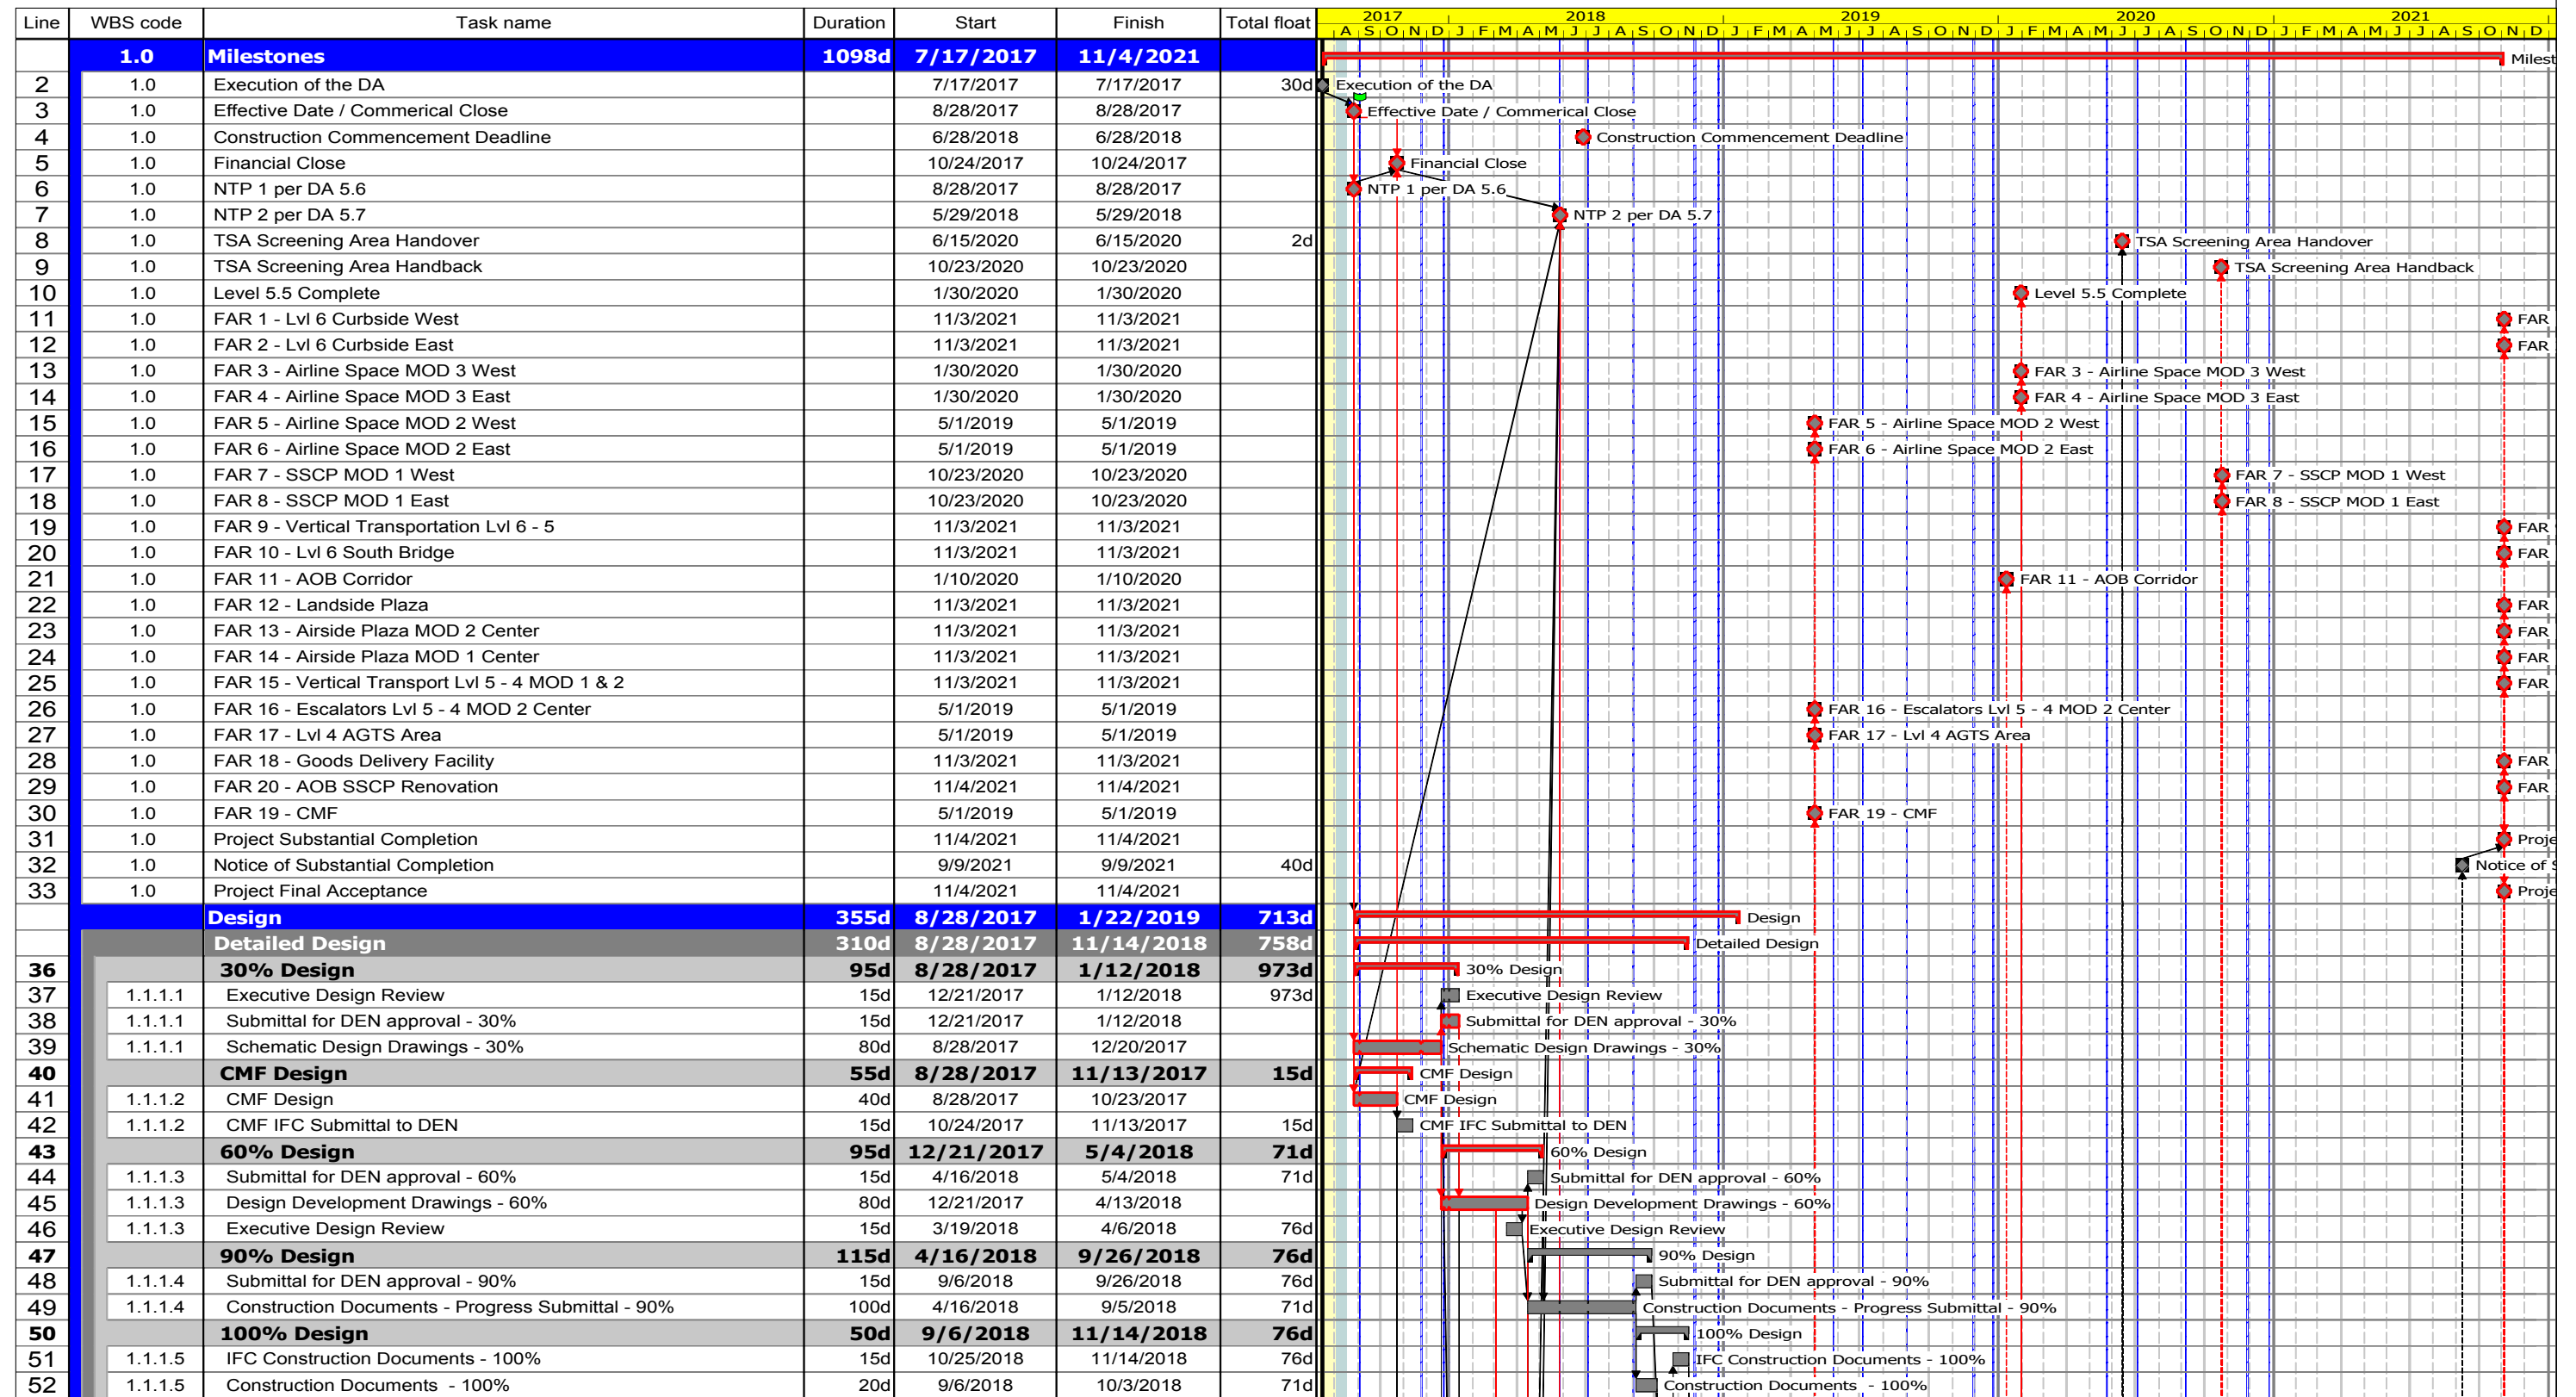

DEN Great Hall

*** Baseline View

Planned by Asta Powerproject

Printed: 7/13/2017

Line	WBS code	Task name	Duration	Start	Finish	Total float	2017												2018												2019												2020												2021											
							A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D							
		Phase 4 - MOD 1 & 3	265d	10/23/2020	11/2/2021	1d																																																												
106		Level 4	170d	10/23/2020	6/22/2021	95d																																																												
107		Level 5	253d	10/23/2020	10/15/2021	13d																																																												
108		Level 6	265d	10/23/2020	11/2/2021	1d																																																												
		Closeout Phase 4 Mod 1&3	16d	10/13/2021	11/3/2021																																																													
		Curbside	100d	10/23/2020	3/16/2021	150d																																																												
		Goods Delivery Structure	160d	3/3/2021	10/12/2021																																																													

