

LAND USE, TRANSPORTATION AND INFRASTRUCTURE COMMITTEE MEETING

MARCH 20, 2018

IMAGINE. DISCOVER. CULTIVATE.







MILESTONES

PREVIOUS 3 MONTHS NEXT 3 MONTHS

- 2018 Stock Show
- Site Plan Completed
- Brighton Blvd NWC
 Construction Started
- NWC Authority Board Convened

- Denver Rock Island Rail Consolidation Design
- Horizontal Designer
- Horizontal Integrated
 Construction Contract
- NWC Initiatives




NWC SITE PLAN

- RTD TRANSIT STATION
- 2 BRIGHTON BLVD. 47TH TO RACE CT.
- SOUTH PLATTE RIVERFRONT
- 4 NEW NAT'L WESTERN DRIVE
- 5 STOCK YARD/EVENT CENTER MULTI-USE SPACE
- ⑥ CAMPUS-RELATED TOD
- NEW BRIDGES NEAR 48TH & 51ST AVENUES
- (E) LIVESTOCK CENTER
- EQUESTRIAN CENTER
- CSU ANIMAL HEALTH FACILITY
- 11 CSU WATER RESOURCE CENTER
- (2) MAINTENANCE & OPERATIONS FACILITY
- (3) DRIR RAIL CORRIDOR
- WSSA LEGACY BUILDING
- (5) PEDESTRIAN BRIDGE
- (B) UNDERGROUND PARKING



LAND ACQUISITION UPDATE

Third Party Number Of Parcels Under Control (Excludes CDOT Land)

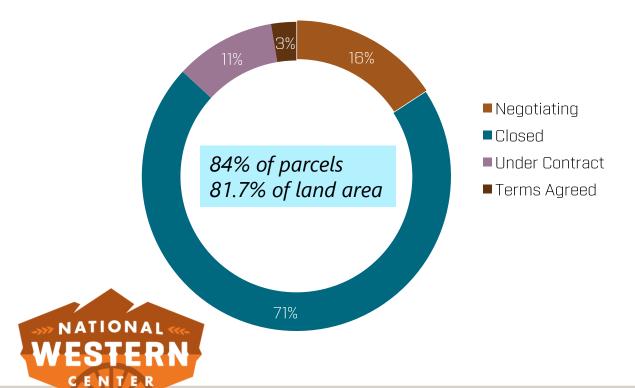

DATE	NUMBER OF PRIVATE PARCELS (38 TOTAL) UNDER CONTROL
Dec 2015	3
Mar 2016	8
Jun 2016	12
Sep 2016	15
Dec 2016	17
Mar 2017	23
Jun 2017	29
Sep 2017	30
Jan 2018	32

PROGRAM CONTROLS: CAPITAL BUILD PHASE 1 & 2 SCOPE

Program-Wide

 Campus planning / placemaking, logistics, public art, insurance, management, contingency

Horizontal Portfolio

• Land and right-of-way acquisition, environmental, sitework, rail consolidation, roads, bridges, utilities, pad-ready sites for partners

Vertical Portfolio

 Demolition, Livestock Center, Equestrian Center, Stockyards Events Center, Stockyards, Cattle Ties, Parking, maintenance building



								Ν	W	'C	CA		TA Desig								E S le Oi		ΗE	Dυ	JLE																			
			016				017					18				201					0 2 0					21				202					23				024				0 2 5	
Program Activities	Q1	Q2	Q3	Q4	Q1	Q2	Q	3 C	ξ4	Q1	Q2	Q3	Q4	ΙQ	1 C	Q2	Q3	Q4	Q1	Q	2 Q	3 C	24	Q1	Q2	Q3	Q4	Q1	. Q	2 C	23	Q4	Q1	Q2	Q3	Q4	l Q1	Q	2 Q3	Q4	Q1	. Q	2 Q	3 Q
Program Milestones																																												
Initial Program Financing										Ш																								į.										
Program Execution and Completion																																			•									
Program and Financial Closeout																																		Ĭ						>				
RTA Completion Deadline										Н																								-¦										-
Program Planning and Preliminary Design																																		İ										
Mobilization																																		- 1										
Site Investigation and Survey																																		-										
Studies and Campus Placemaking																																		į										
Site Infrastructure																																		-										
Land Acquisition									4																																			
Main Access Road and Utilities							Brigh	nton B	lvd																									ij										
Demolition and Abatement																																		- 1										
Rail Consolidation							\top																											- i										
DPS Environmental Remediation										П																																		
Site Clearance, Earthwork and Grading										П																								i,										
Campus Roads and Utilities										П																																		
Bridges and Tunnels																												-						į										
NWC Grounds										Н																								+										
New At-Grade Stockyards										П				4													_																	
Cattle Tie Area														Т																				- 1										
Riverfront Open Space				16	.3	%														H														÷										
NWC Venues			C	on	าต	lei	te		-																									+										
Stockyards Event Center																																												
Livestock Center			(in	clu	des	s la	nd																																					
Equestrian Center / Parking Garage				cqı																														-										
NWC Other Facilities										П																								İ										
Maintenance and Operations Building															+	-																		-										
Main Campus Plaza	-		On	S	che	ed	ul	е															+											÷										
NWC Partners - Pad-Ready Sites									7																									Ī										
Water Resources Center (CSU and DW)										Ш							\																	4										
Animal Health Facility (CSU)										\vdash									\												-			÷										
NWC Partners - Future Development Sites																																												
CSU WRC (Timing TBD)																																												
CSU Animal Health Clinic (Timing TBD)																																												
WSSA Legacy Building (Timing TBD)																																												

PROGRAM CONTROLS: FINANCIAL UPDATE

Budget, Commitment and Cost – Through January 2018 (\$ Million):

Scope	Budget	Committed	Expended
Horizontal	\$375.6	\$ 135.9	\$112.9
Vertical	\$305.9	\$ 0.9	\$ 0.0
Program-Wide	\$ 84.0	\$ 17.1	\$ 5.9
Total	\$765.5	\$153.9	\$118.8
% of Budget		20.1%	15.5%
Thru Q3 2017	\$765.0	\$115.6	\$ 81.3



COMMUNICATIONS: TEXTING

SIGN UP FOR TEXT MESSAGE UPDATES

GET UPDATES ABOUT THE NATIONAL WESTERN CENTER RIGHT ON YOUR PHONE!

Text the word **CONSTRUCTION** to **64600** to receive information on construction, road closures, and project updates. Text the word **UPDATES** to **64600** to hear about upcoming outreach and community events.

¡RECIBE ACTUALIZACIONES EN TU CELULAR SOBRE EL NATIONAL WESTERN CENTER!


Envía la palabra CONSTRUCCION al 64600 para actualizaciones sobre calles cerradas y el proyecto de construcción. Envía la palabra NOTICIAS al 64600 para información de los próximos eventos y actividades para la comunidad.





IMAGINA. DESCUBRE. CULTIVA.




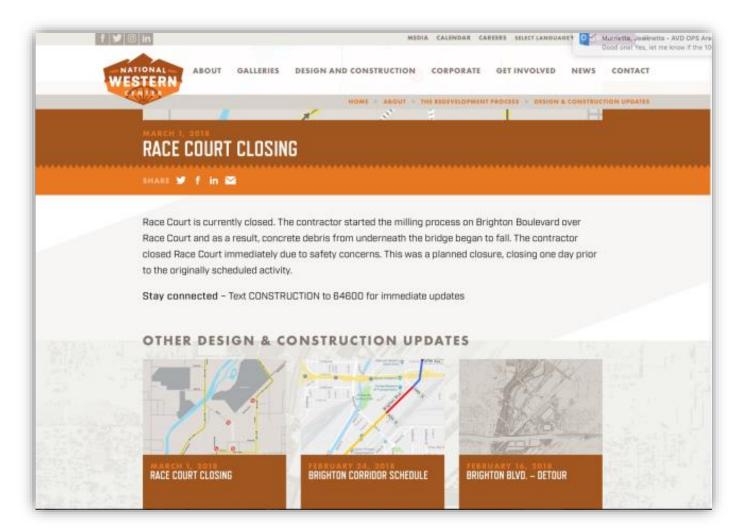








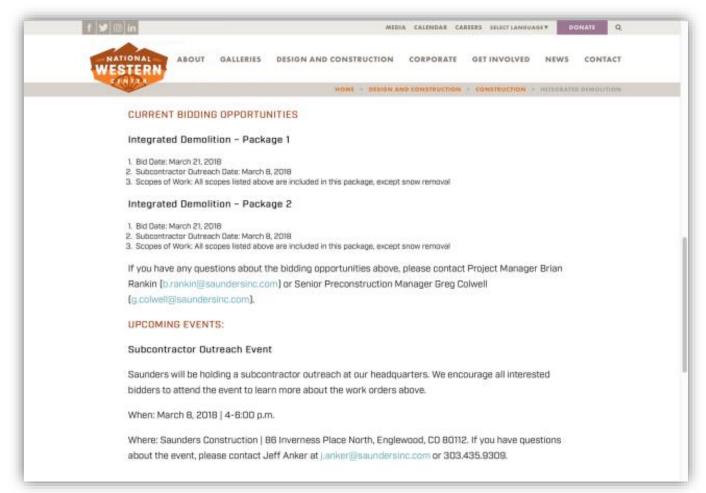



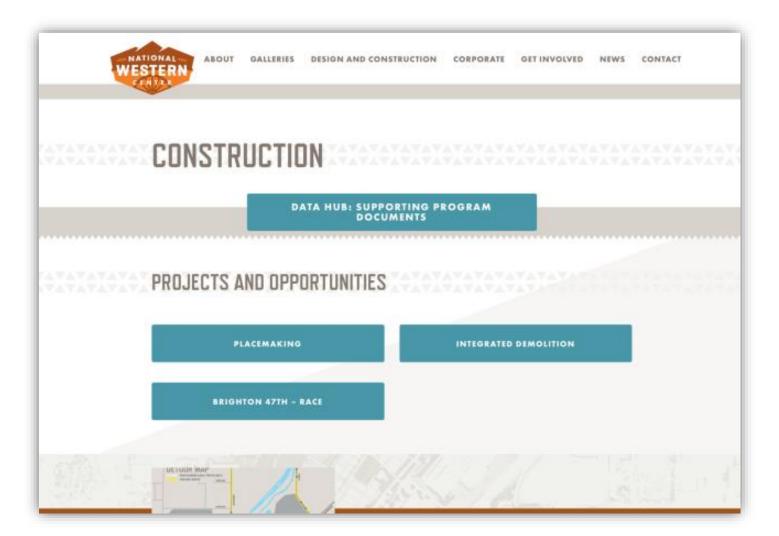







WORK UNDERWAY

CAMPUS PLACEMAKING STUDY

MIG

M/WBE GOAL: 24%

Scope	Status					
Program Refinement	Ongoing					
Market Analysis	Ongoing					
Built Form, Campus Character And Campus Cultural Plans	Ongoing					
15-30% Infrastructure Design	Ongoing					
Public Realm Study	Start April 2018					
Design Standards And Guidelines	Start June 2018					

INTEGRATED DEMOLITION

SAUNDERS CONSTRUCTION

M/WBE GOAL: 24%

Scope	Status
Property and Project Management	Ongoing
Demolition Bid Package #01	Currently Bidding/Start April 2018



ACTIVE PROCUREMENTS

CONTRACT	SCOPE OVERVIEW	INFORMATION
DRIR RAILROAD	 Design of the Denver Rock Island Railroad (DRIR) rail consolidation, 	Type: Professional Services contract
CONSOLIDATION DESIGN	including:	Status: In City Council Process
	 Relocate tracks through the NWC Campus 	Start: April 2018
	 New / relocated maintenance facility to enable the Capital Build 	Amount: \$2.19M (capacity)
		Goal: 14%
HORIZONTAL INTEGRATED CONSTRUCTION SERVICES	 Integrated Construction services contractor for campus-wide horizontal elements: 	Type: Construction Services contract (Work Order Based)
	Enabling WorksSite Wide Infrastructure / RoWs	Status: Interviews (Council Process - May 2018)
	DPS Site StabilizationBridge Structures	Start: June 2018
	 DRIR Rail Consolidation Riverfront Open Space 	Amount: \$275M (capacity)
	 "Pad-ready" sites for CSU, WSSA 	Goal: Work Order By Work Order Basis

ACTIVE PROCUREMENTS

eer-of-Record for campus-wide ontal design, including:	Type: Professional Services contract (Task Order Based)
ing Works Vide Infrastructure / RoWs Site Stabilization e Structures Rail Consolidation front Open Space ready" sites for CSU, WSSA	Status: Merrick & Company pending Council Approval - March 2018 Start: April 2018 Amount: \$25M (capacity) Goal: 23%
	intal design, including: ing Works /ide Infrastructure / RoWs Site Stabilization e Structures Rail Consolidation front Open Space



HORIZONTAL DESIGNER

HORIZONTAL PORTFOLIO DESIGNER: PURPOSE & SCOPE OF SERVICES

- Single point control and Engineer of Record for all necessary professional and design services to provide and implement campus-wide Horizontal Portfolio Design packages.
- Provide 'For Construction' drawings and specifications to the Horizontal Integrated Construction Services Contractor (HIC) for construction and provide construction support services to the HIC.
- Scope Elements Include: Site wide infrastructure to include utilities, and roads, riverfront open space, environmental clean-up, bridge structures and 'pad ready' sites for venue construction, including the Colorado State University and Western Stock Show Association venues.

KEY CONTRACT INFORMATION

Recommended Award: Merrick & Company

Contract Type: Task Order Based Contract Capacity: \$ 25 mil

M/WBE: 23%

Anticipated Contract Duration: 5 Years Anticipated Design Start: April 2018

Procurement Process: Two Step (RFQ/RFP with Interviews)



HORIZONTAL DESIGNER

PROCUREMENT PROCESS OVERVIEW

Request for Qualifications (RFQ) Advertisement:

Pre-Submittal Meeting:

Submittals Due:

Shortlist Notified:

Request for Proposal (RFP) Issued:

Pre-RFP Meeting:

Interviews:

Selection Committee Recommended Award:

October 16, 2017
October 30, 2017
November 17, 2017
December 19, 2017
December 22, 2017
January 8, 2018
February 1, 2018
Merrick & Company



FUTURE 2018 VERTICAL PROCUREMENTS

PROCUREMENT PACKAGE	Service	2018	2019
Stockyards Event Center & Stockyards	Design	Start Design	November 2018
	CM/GC		Start Pre-Con February 2019
Maintenance & Operations Facility	Design	★ Start Design	September 2018
	CM/GC	★ Start Pro	e-Con November 2018
Equestrian Center & Parking Garage	Design		Start Design April 2019
	CM/GC		Start Pre-Con July 2019



Design - Procurement Duration

CM/GC - Procurement Duration

PROGRAM UPDATE: FUTURE 2018 PROCUREMENTS

CENTER

	CONTRACT	SCOPE OVERVIEW	INFORMATION
	MAINTENANCE AND OPERATIONS FACILITY DESIGN	Design of the Maintenance and Operations Facility Renovation, including: • Maintenance and Vehicle Shops with Yard • Equipment and Material Storage • Cattle Tie Areas for Annual Stock Show	Type: Professional Services Status: Release RFQ May 2018
	CONSTRUCTION	Construction of the Maintenance and Operations Facility Renovation, including: • Maintenance and Vehicle Shops with Yard • Equipment and Material Storage • Cattle Tie Areas for Annual Stock Show	Type: CM/GC Status: Release RFQ June 2018 (Council Process Oct 2018) Start: November 2018 (Pre-Construction Services)
->	NATIONAL		Amount: TBD Goal: TBD

PROGRAM UPDATE: FUTURE 2018 PROCUREMENTS

CONTRACT	SCOPE OVERVIEW	INFORMATION
STOCKYARDS AND STOCKYARD EVENT CENTER DESIGN	 Design of the Stockyard and Stockyards Event Center, including: 20 acres of Stockyards with 800+ removable pens Catwalks and building terraces Multi-use events and festival space during non-Stock Show times Stockyards Event Center facility, including a 1000-seat Arena with 2 show rings and a 600-seat Auction Arena 	Type: Professional Services Status: Release RFQ June 2018 (Council Process Oct 2018) Start: November 2018 Amount: TBD Goal: TBD
CONSTRUCTION	Construction of the Stockyard and Stockyards Event Center, including: 20 acros of Stockyards with 200+ removable	Type: CM/GC Status: Release RFQ July 2018 (Coupeil Process, Dec 2019)



- 20 acres of Stockyards with 800+ removable pens
- Catwalks and building terraces
- Multi-use events and festival space during non-Stock Show times
- Stockyards Event Center facility, including a 1000-seat Arena with 2 show rings and a 600-seat Auction Arena

(Council Process Dec 2018)

Start: February 2019 (Pre-Construction Services)


Amount: TBD

Goal: TBD

FUTURE 2018 PROCUREMENTS

CENTER

CONTRACT	SCOPE OVERVIEW	INFORMATION				
EQUESTRIAN CENTER AND PARKING GARAGE DESIGN	 Design of the Equestrian Center and Parking Garage, including: 4,500 Seat Event Center 500 Equestrian Show Arena 700-800 stall Horse Barn Two Paddocks and Covered Open-Air Warm Up areas 1,050 car Parking Garage 	Type: Professional Services Status: Release RFQ October 2018 (Council Process Feb 2019) Start: April 2019 Amount: TBD Goal: TBD				
CONSTRUCTION	 Construction of the Equestrian Center and Parking Garage, including: 4,500 Seat Event Center 500 Equestrian Show Arena 700-800 stall Horse Barn Two Paddocks and Covered Open-Air Warm Up areas 1,050 car Parking Garage 	Type: CM/GC Status: Release RFQ Dec 2018 (Council Process May 2019) Start: July 2019 (Pre-Construction Services) Amount: TBD Goal: TBD				





1909 HISTORIC BUILDING STUDY

Can We Adaptively Reuse The 1909 Stadium Arena As Denver's First Public Market?

- Establish Advisory Working Group
- Historic Structure Assessment
- Economic Feasibility Study
- Preferred Development Program

- **Business Plan**
- Partnership/governance recommendations











HISTORIC RESOURCES - 2018 OVERVIEW

- Historic Resources process and overall campus strategy
 - Work session with History Colorado, Historic Denver, Landmark Preservation
 - Includes historic buildings and other historic site resources
- Cataloging of site historic elements
 - Images and GPS location of all key historic elements
- Development of Campus Cultural Plan (Campus Placemaking)



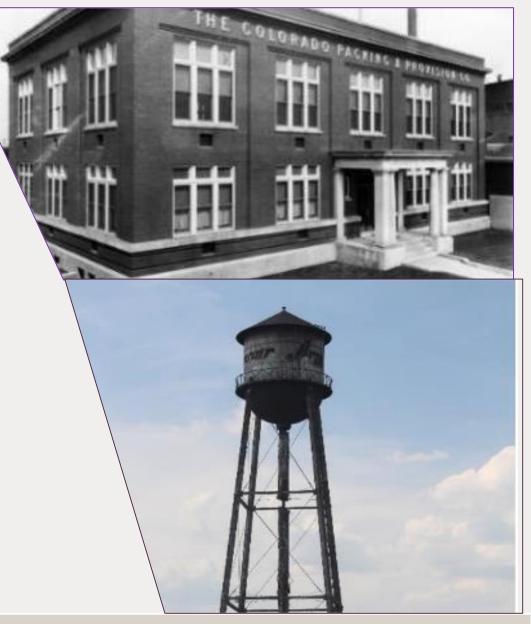

CAMPUS ENERGY UPDATE

MEETING NWC ENERGY GOALS THROUGH PARTNERSHIPS

- NWC Master Plan envisions a "Net Zero Energy District"
- Request for Information (RFI) = "Market Research" to inform procurement
- Very positive market response
 - Global expertise
 - Equity investment
 - Comparable energy costs to "business as usual" (grid)
 - Collaboration with Xcel/Metro Wastewater
 - Primary recommended technologies:
 - On-site / Off-site solar
 - District energy utilizing heat from the Delgany Interceptor





METRO WASTEWATER PARTNERSHIPS

DELGANY INTERCEPTOR RELOCATION

- December 2016: NWCO signs MOU with Metro Wastewater
- July 2017: Delgany / Sewer Heat Recovery Study Completed
- March 2018: Technical Memo and Cost Estimate
- April 2018: IGA
 - Pipeline relocation and burial
 - Biofilter
 - > Tie-ins with Denver WW pipelines





TRIANGLE @ NATIONAL WESTERN CENER

A call to all trailblazers in agriculture, water and food science research

The National Western Center <u>brings together global thought leaders</u>, curious students, and local community at an intersection of agriculture, education and entertainment.

We are creating a **pioneering space to connect** agriculture researchers, industry leaders and entrepreneurs.

By bringing together this expertise to engage and explore, we offer a place where innovators can develop new technologies for providing healthy food and clean water.



ROLES & RESPONSIBILITY FOR THE TRIANGLE @ NWC



Principal land and facility owner, leading the procurement process to select a development partner



National Western Center Authority

Non-profit Colorado corporation with 100year lease for the campus; responsible for bookings, long-term operations and maintenance



100-year lease with NWC Authority; produces the National Western Stock Show, Rodeo All-Star Weekend, and Denver County Fair; books other year-round equestrian and livestock events with the Authority; parcel owner for the Legacy Building



Independent parcel owner of the funded CSU educational facilities (Water Resources Center, Animal Health, CSU Center); provides year-round educational programming





Programming Partners



OPPORTUNITY FOR INNOVATION


60 total acres with 18 acres reserved for:

Required Assets:

- New 10,000-seat Arena
- Redeveloped historic 1909 Building
- New Expo Hall
- · and supporting structured parking

A parcel reserved for funded CSU Center

- Adjacent to new commuter rail station
- Additional 42 acres available for supporting development (retail, hospitality office, housing), including the decommission and reuse of the Coliseum site

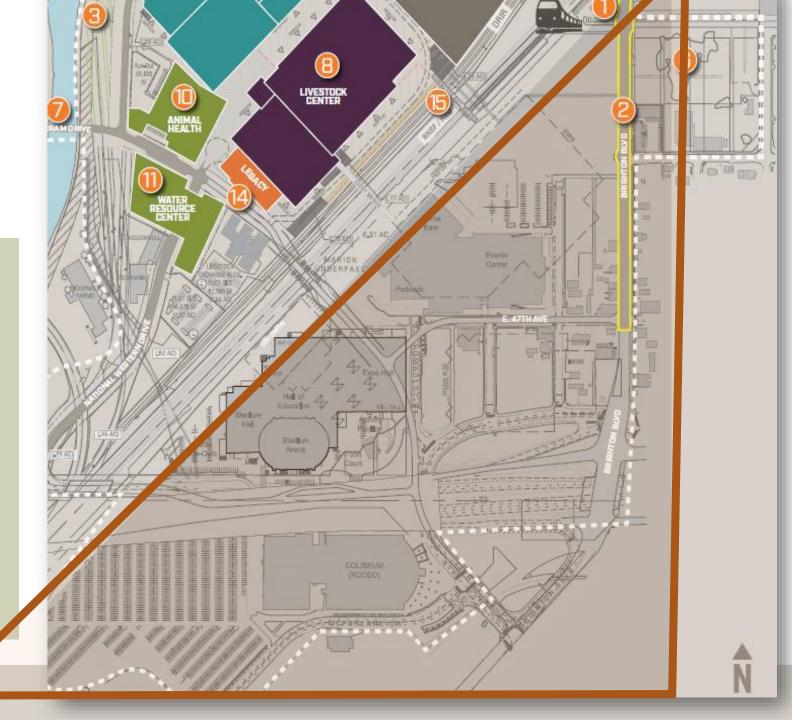

ASSETS TO BE DEVELOPED

Approximately 18 acres for required assets with estimated sizes and costs are shown at right.

Approximately 42 acres for additional optional elements including potential for retail, hospitality, office, and housing.

An additional parcel reserved for fully funded \$50 million CSU Center.

Required Assets Approx. 18 Acres	Approximate Square feet	Spaces	Estimated Cost per	Estimated Construction Totals
New Arena	295,000		\$400/SF	\$120 million
Expo Hall	460,000		\$270/SF	\$125 million
1909 Building Restoration	45,000		\$300/SF	\$15 million
Structured Parking		2000	\$25K / space	\$50 million
Additional Private Sector Opportunities Approx. 42 Acres	Estimated Market (SF)	Units / Keys	Estimated Cost per	Estimated Construction Total
Retail	105K-170K		\$125 / SF	\$13 - \$21 million
Hospitality	100K-160K	140-245 keys	\$200K / key	\$28 - \$49 million
Office	300K-550K		\$300 / SF	\$90 - \$165 million
Housing	200K-400K	200-400 units	\$265/SF	\$53 - \$106 million
Total 	1.5 - 2 million			\$495 - \$650 million



THANK YOU! QUESTIONS?

